


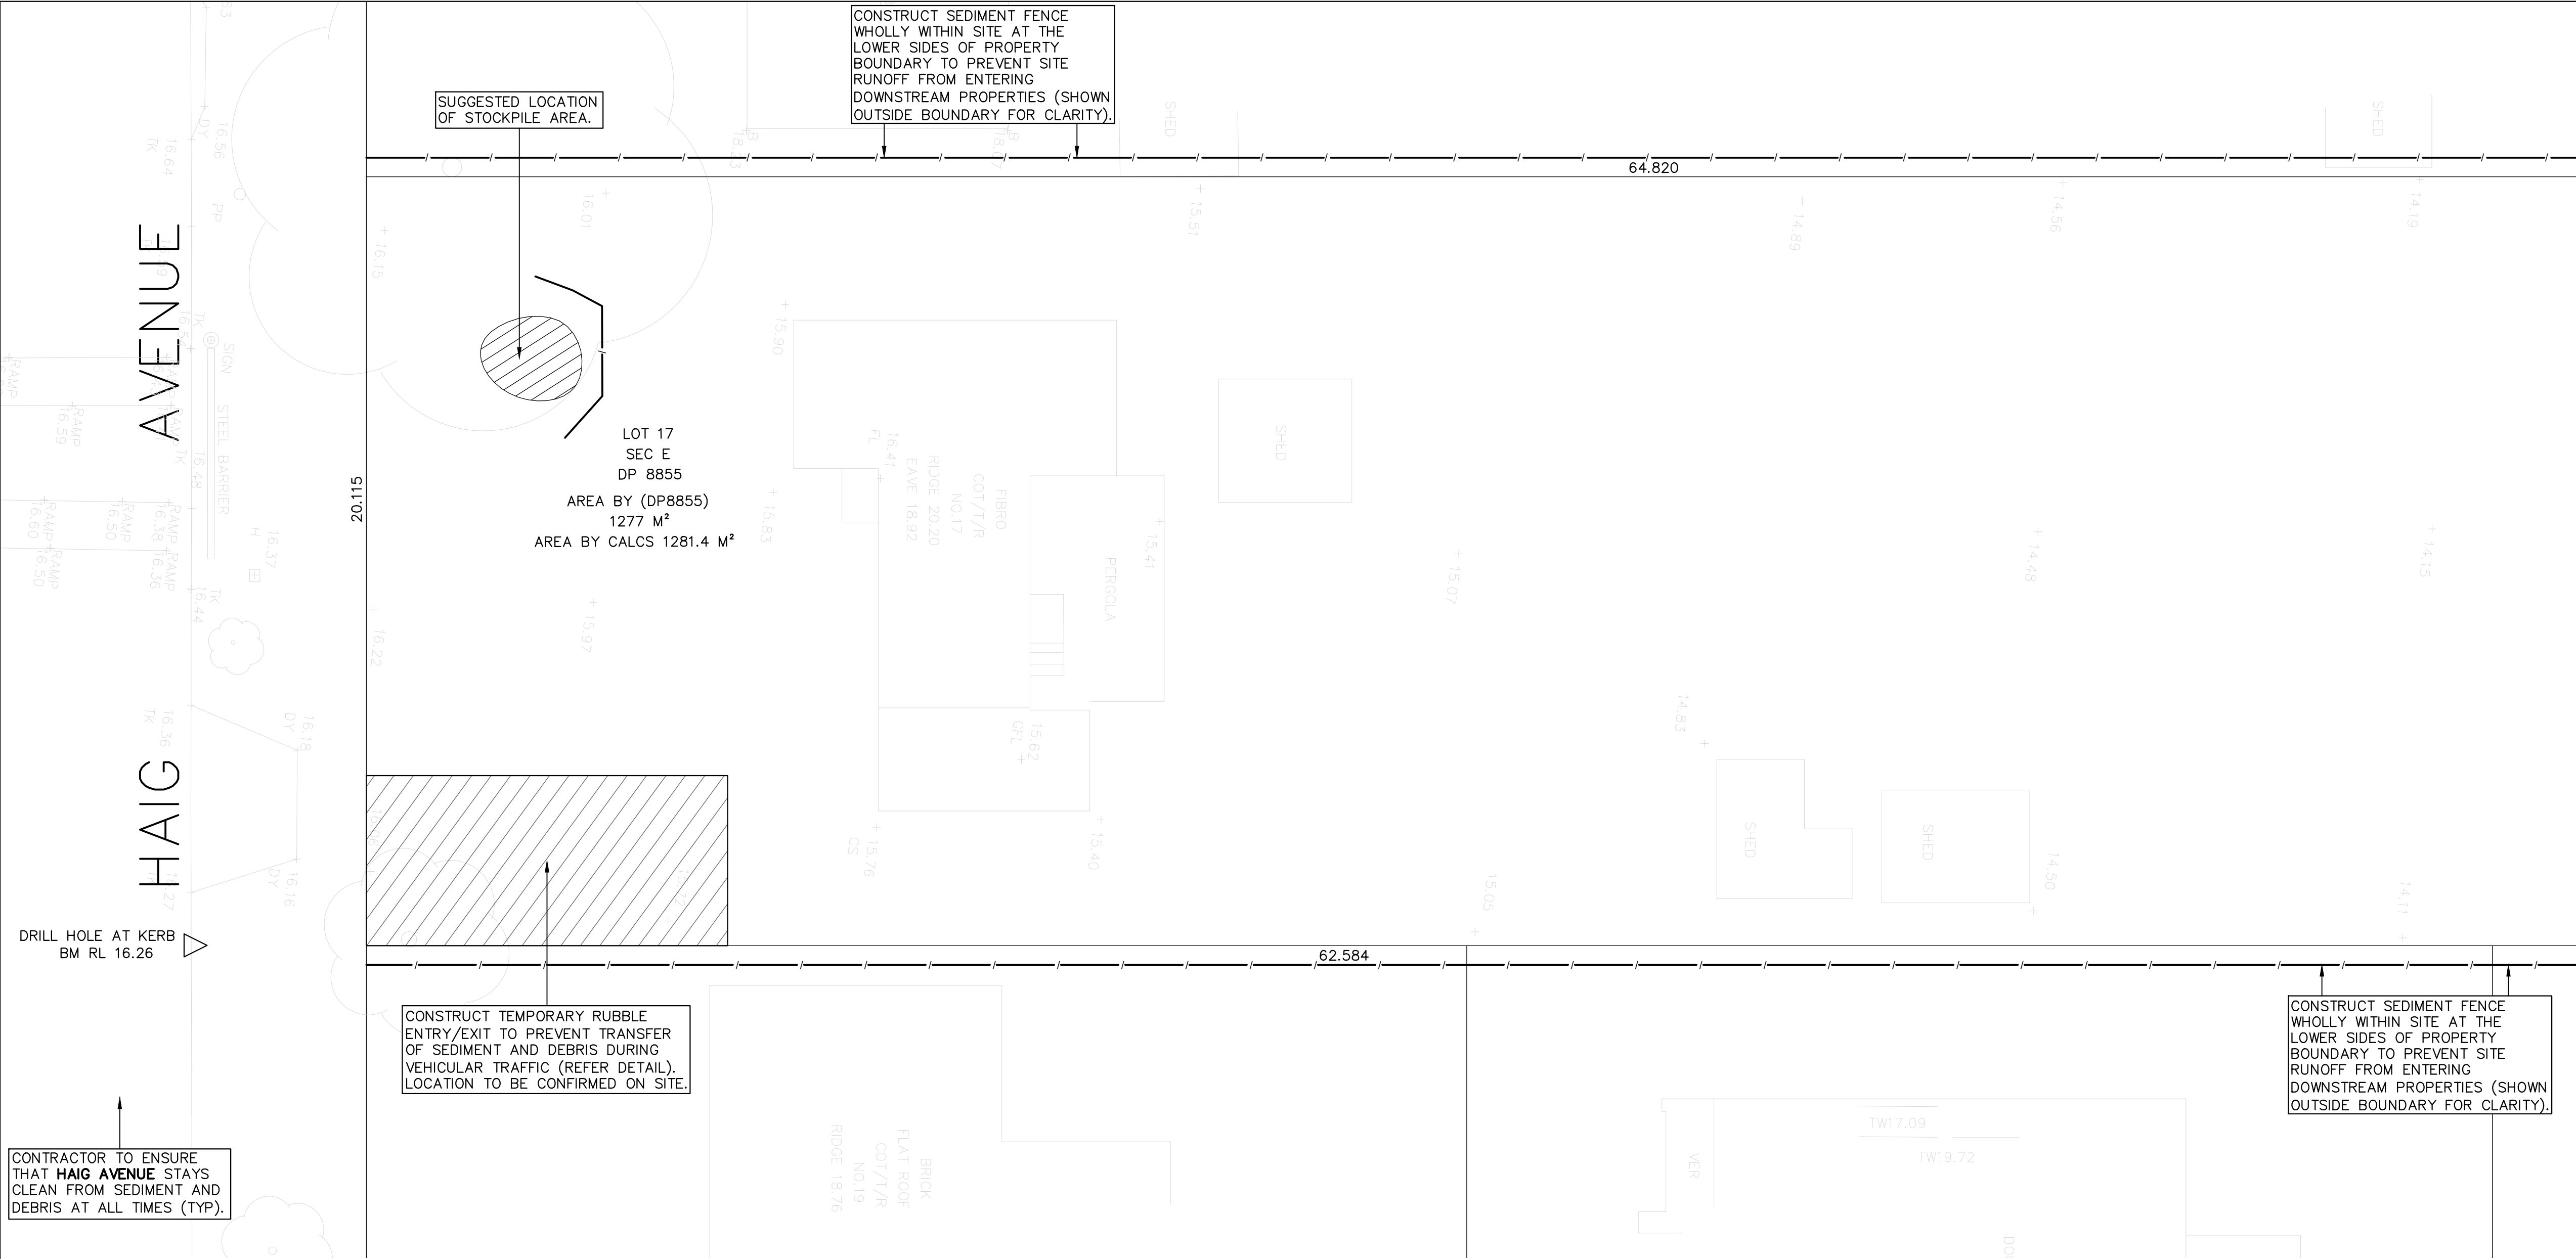

EROSION CONTROL

BEFORE EARTHWORKS CAN COMMENCE THE EROSION & SEDIMENT CONTROL MEASURES MUST BE IN PLACE.

DURING THE CONSTRUCTION PERIOD, THESE CONTROL MEASURES WILL NEED TO BE INSPECTED & MAINTAINED REGULARLY, ESPECIALLY AFTER STORM EVENTS, BY THE CONTRACTOR.

ALL WORK IS TO BE CARRIED OUT TO PREVENT EROSION, CONTAMINATION & SEDIMENTATION OF THE STORAGE SITE, SURROUNDING AREAS & DRAINAGE SYSTEMS.

MINIMIZE DISTURBED AREA COVERED WITH NATURAL VEGETATION. ONLY THOSE AREAS DIRECTLY REQUIRED FOR CONSTRUCTION ARE TO BE DISTURBED.

ISOLATE EXISTING STORMWATER PITS WITH STRAW BALES OR SILT TRAPS TO FILTER ALL INCOMING FLOWS.

DO NOT STOCKPILE EXCAVATED MATERIAL ON THE ROAD WAY.

DIVERT CLEAN WATER FROM UNDISTURBED AREAS AROUND THE WORKING AREAS.

CONSTRUCTION ENTRY/EXIT SHALL BE VIA THE LOCATION NOTED ON THE DRAWING. CONTRACTOR SHALL ENSURE ALL DROPPABLE SOIL & SEDIMENT IS REMOVED PRIOR TO CONSTRUCTION TRAFFIC EXITING SITE. CONTRACTOR SHALL ENSURE ALL CONSTRUCTION TRAFFIC ENTERING AND LEAVING THE SITE DO SO IN A FORWARD DIRECTION.

ADOPT TEMPORARY MEASURES AS MAY BE NECESSARY FOR EROSION & SEDIMENT CONTROL, INCLUDING BUT NOT LIMITED TO THE FOLLOWING:

- DRAINS: TEMPORARY DRAINS AND CATCH DRAINS.
- SPREADER BANKS OR OTHER STRUCTURES: TO DISPERSE CONCENTRATED RUNOFF.
- SILT TRAPS: CONSTRUCTION AND MAINTENANCE OF SILT TRAPS TO PREVENT DISCHARGE OF SCOURED MATERIAL TO DOWNSTREAM AREAS.


AFTER RAIN, INSPECT, CLEAN, AND REPAIR IF REQUIRED, TEMPORARY EROSION & SEDIMENT CONTROL MEASURES.

REMOVE TEMPORARY EROSION & SEDIMENT CONTROL MEASURES WHEN THEY ARE NO LONGER REQUIRED.

COMPLY WITH THE REQUIREMENTS OF LANDCOM'S MANAGING URBAN STORMWATER – SOIL AND CONSTRUCTION 'THE BLUE BOOK' LATEST EDITION


THE EROSION & SEDIMENT CONTROL PLAN PROVIDED IS ONLY INDICATIVE. THE CONTRACTOR SHOULD PREPARE A DETAILED ESCP SUITABLE FOR THE SPECIFIC SITE CONDITIONS

EROSION & SEDIMENT CONTROL PLAN
SCALE 1:100

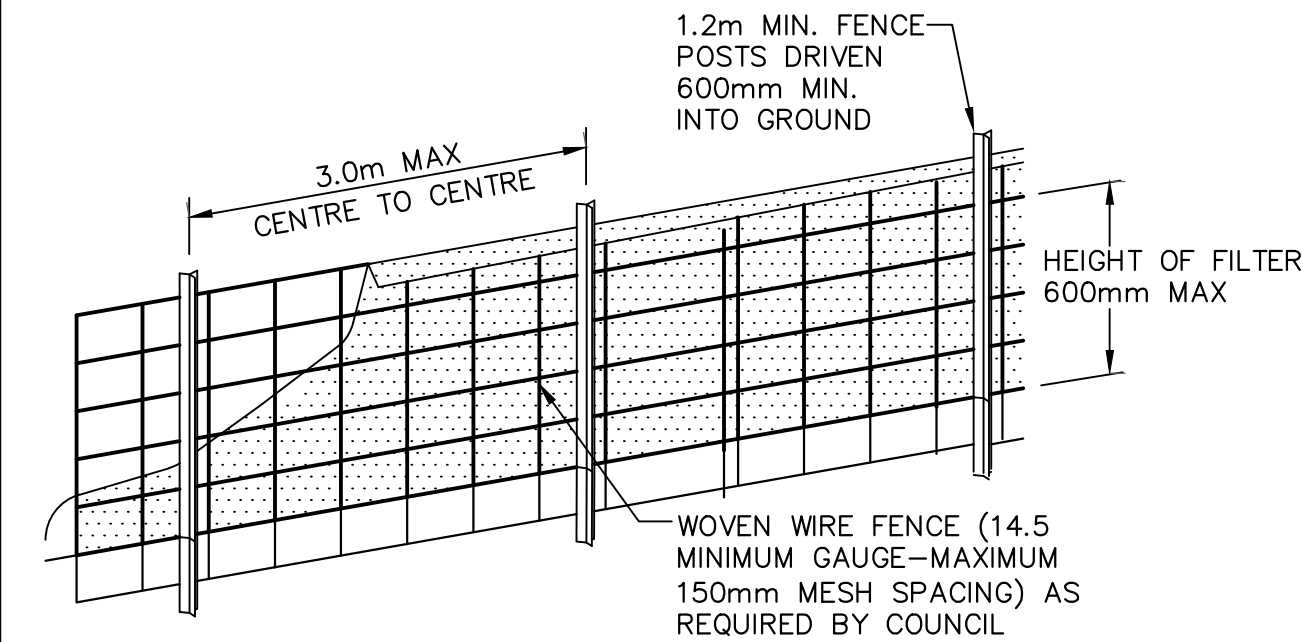


DIAGRAMMATIC VIEW



SEDIMENT FENCE DETAIL
NOT TO SCALE

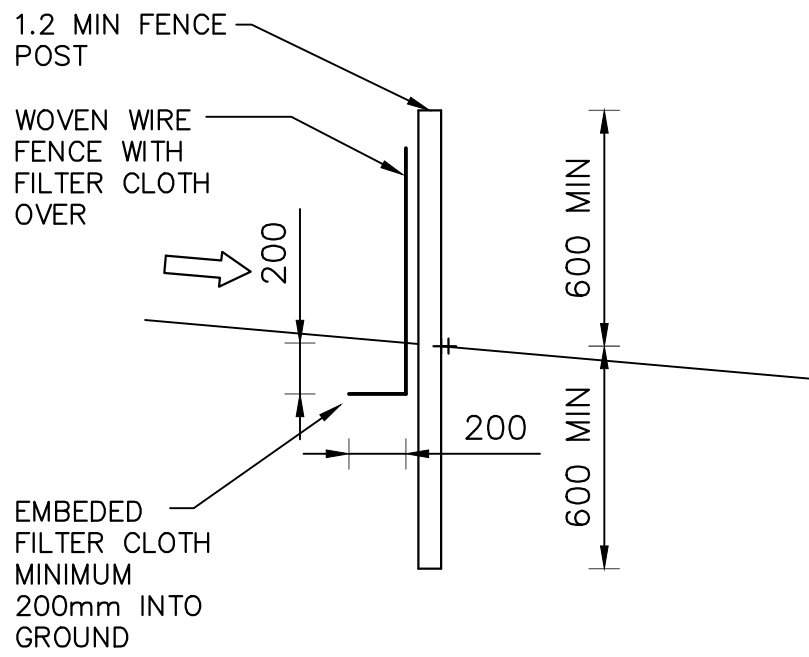

TYPICAL SECTION

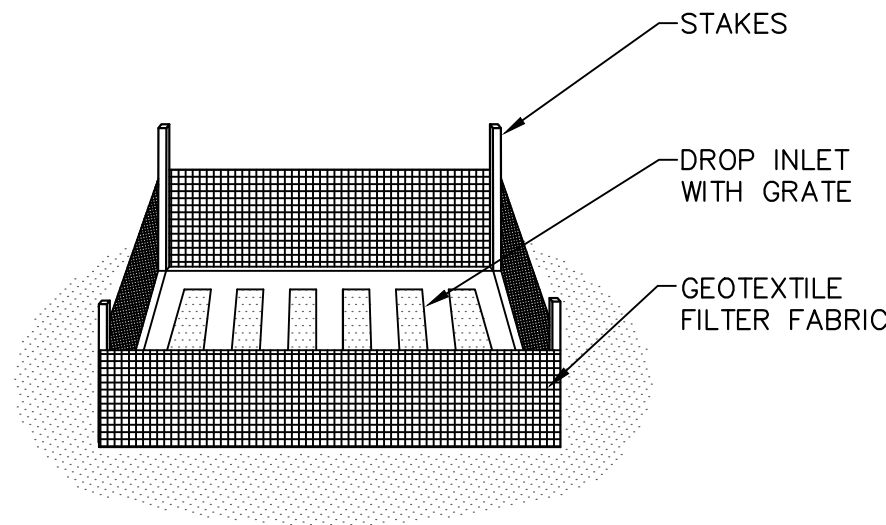


SUMP SEDIMENT TRAP DETAIL
NOT TO SCALE

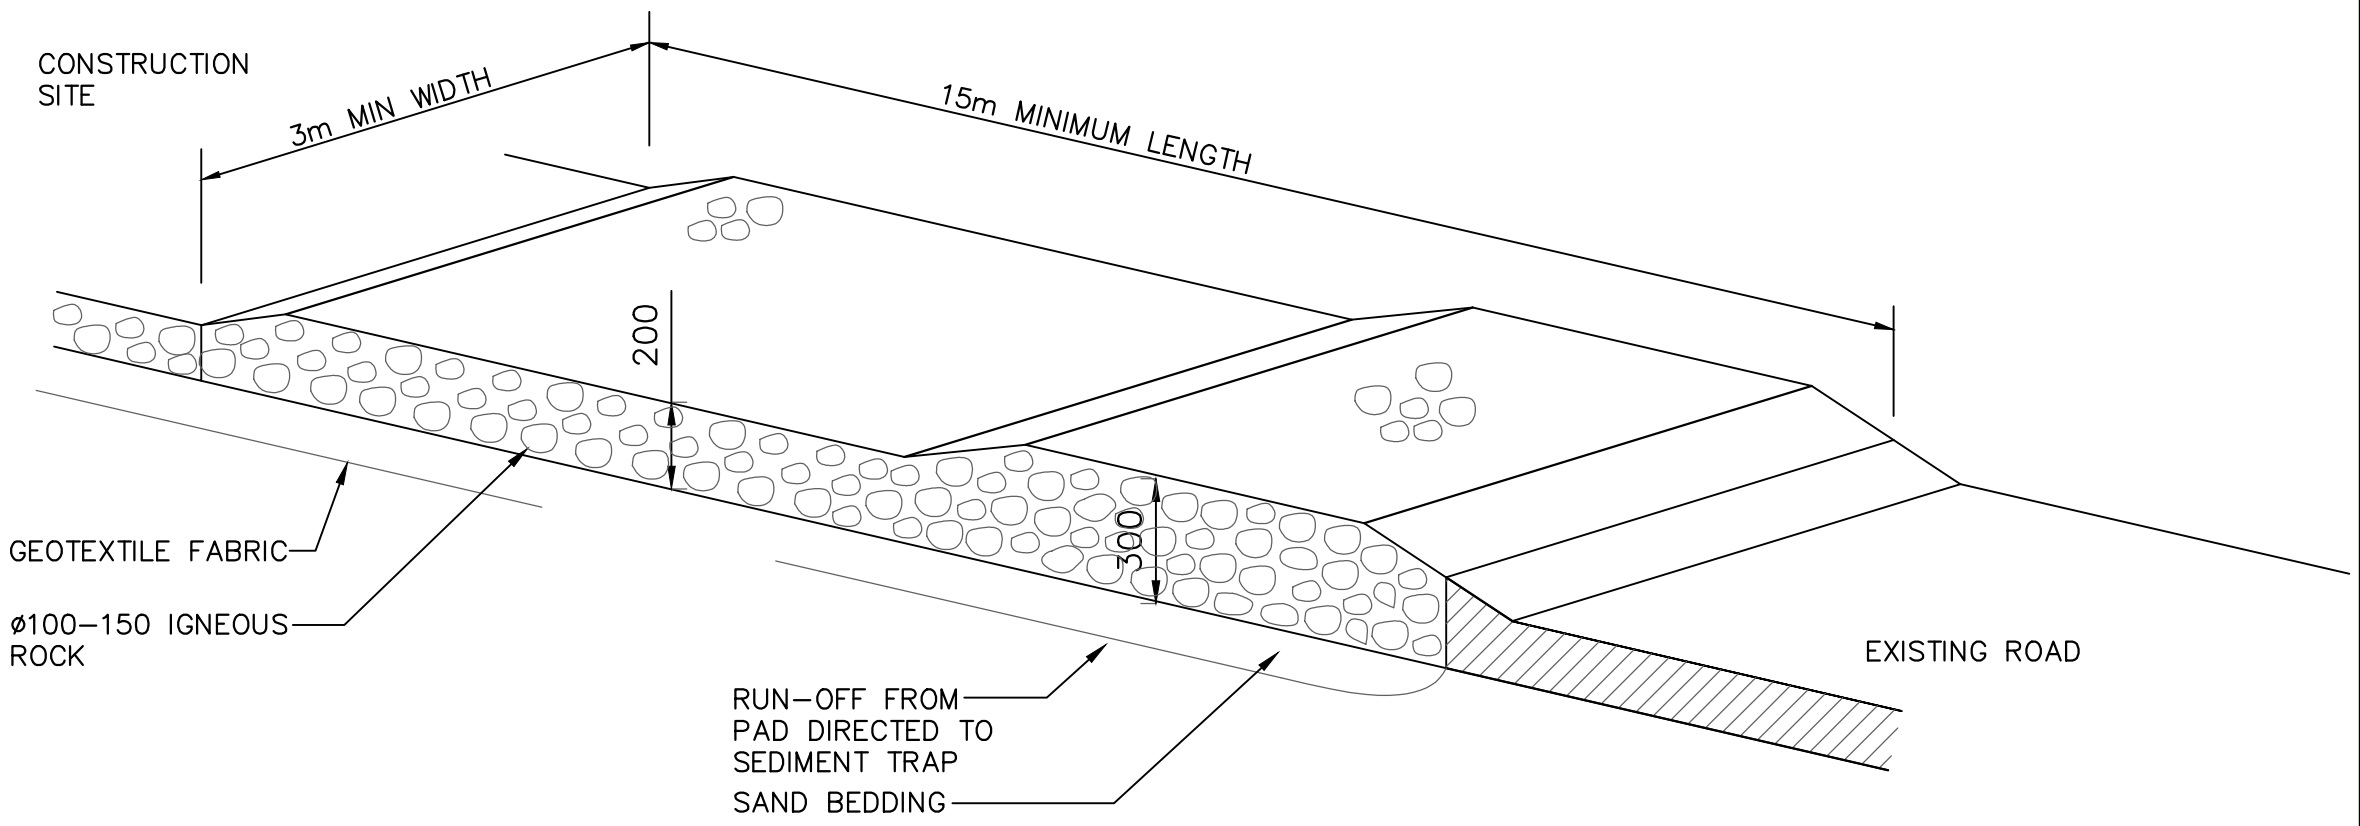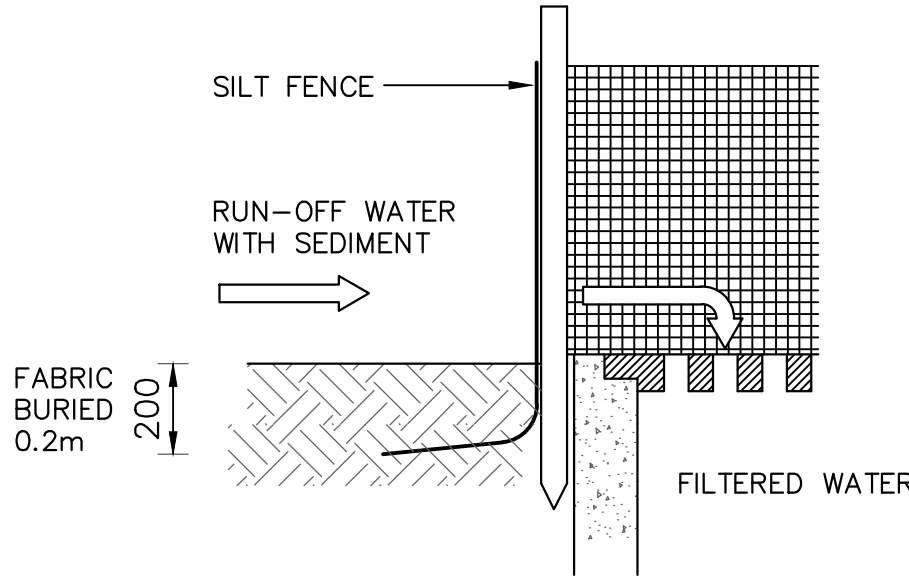

TEMPORARY CONSTRUCTION EXIT (RUBBLE ALTERNATIVE)
NOT TO SCALE

ISSUED FOR D.A.

A1										E: ahmad@nceeng.com M: 0452489806 COPYRIGHT THIS DRAWING AND THE INFORMATION SHOWN HEREIN IS THE PROPERTY OF NANO CONSULTING ENGINEERS AND MAY NOT BE USED FOR ANY PURPOSES THAN FOR WHICH SUPPLIED.																				DRAWN : A.N. DESIGNED : A.N. REVIEWED : A.N. DATE : 05/06/2026 CHECKED : A.N. APPROVED DATE : 05/06/2026																				ARCHITECT: PALADEUM DESIGN STUDIO										CLIENT: PALADEUM DESIGN STUDIO										PROJECT : PROPOSED DUPLEX ADDRESS : 17 HAIG AVE, GEORGES HALL NSW APPLICATION : DA LGA : CANTERBURY-BANKSTOWN COUNCIL										SHEET SUBJECT : EROSION & SEDIMENT CONTROL PLAN, NOTES & DETAILS																				ALL DIMENSIONS IN mm UNLESS OTHERWISE STATED DO NOT SCALE DRAWINGS, USE FIGURED DIMENSIONS ONLY																			
A										FOR DA APPROVAL										A.N.										A.N.										05/06/2026										APPROVAL TYPE: 1. PRELIMINARY 2. DEVELOPMENT APPLICATION 3. CONCEPT DEVELOPMENT 4. CONSTRUCTION SERVICES 5. FOR TENDER 6. OTHER										ADDRESS : 5 BURROWS AVENUE, CHESTER MILL Ph: 0452489806 EMAIL: ahmad@nceeng.com																														SCALE @ A1 1:100										JOB No SW26149																			
REV										DESCRIPTION										BY										CHECK										DATE																																																		AUTHORISED A.N.										DWG No ER001										REV A									
